Mainframe OS Upgrade
Project Schedule

Gantt Chart
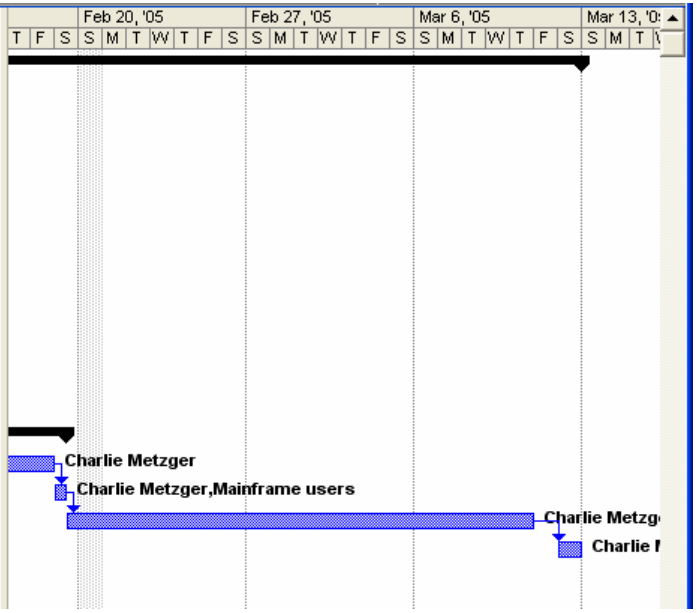
	Task Name	Duration	Start	Finish	Predecessors
1	**Mainframe OS Upgrade**	**208 days**	**Mon 7/5/04**	**Sat 3/12/05**	
2	Initial Installation of z/OS 1.4	21 days	Mon 7/5/04	Mon 8/2/04	
3	**Verification and testing in test partition**	**70 days**	**Tue 8/3/04**	**Mon 11/8/04**	
4	Verify z/OS 1.4 Installation in test partition	15 days	Tue 8/3/04	Mon 8/23/04	2
5	Customize and testing in test partition	20 days	Tue 8/24/04	Mon 9/20/04	4
6	Test core OS functionality in test partition	5 days	Tue 9/21/04	Mon 9/27/04	5
7	Migrate, customize and test OS subsystems	30 days	Tue 9/28/04	Mon 11/8/04	6
8	Migrate, customize and test ISV software	30 days	Tue 9/28/04	Mon 11/8/04	6
9	**Verification and testing in production partition**	**82 days**	**Sat 11/13/04**	**Sun 2/6/05**	
10	**Test core OS functionality during weekend downtime**	**24 days**	**Sat 11/13/04**	**Mon 12/6/04**	
19	**Test OS subsystems & ISV software during weekend downtime**	**9 days**	**Sat 12/11/04**	**Sun 12/19/04**	
24	**Test CICS and DB2 during weekend downtime**	**9 days**	**Sat 1/8/05**	**Sun 1/16/05**	
29	**Test SCT software & systems during weekend downtime**	**16 days**	**Sat 1/22/05**	**Sun 2/6/05**	
36	**General User Testing**	**10.5 days**	**Mon 2/7/05**	**Sat 2/19/05**	
37	Prepare z/OS 1.4 for general user testing in production partition	10 days	Mon 2/7/05	Fri 2/18/05	29
38	General user preview and test	0.5 days	Sat 2/19/05	Sat 2/19/05	37
39	Final Preparations	18.5 days	Sat 2/19/05	Thu 3/10/05	38
40	Go Live with z/OS 1.4	1 day	Sat 3/12/05	Sat 3/12/05	39
